

Hood River County School District – 2016 Bond Projects

Bond Projects Report September 2018



Wy'east Middle School



- New replacement reader board to be installed.
- Field goal posts from HRVHS re-installed for continued use.



Wy'east Middle School (Seismic)

- Seismic scope is substantially complete. Punchlist work in process.
- Accounting package underway for grant reimbursement.



Hood River Options Academy Remodel



- Demolition and abatement has been completed.
- Framing complete. Mechanical and electrical rough-in underway.
- Hood River Options Academy completion is scheduled for mid-Fall.



May Street Elementary School



- All slab-on-grade pours have been completed.
- Steel erection is on-going. Sector A has been completely erected.
- Next Sector steel is on site.



May Street Elementary School



MAY STREET ELEMENTARY SCHOOL September Construction Update

Work Completed

- Stem walls poured for the gym and administration area
- Slab preparation for concrete pour
- Steel erection has begun!



Steel erection at NE corner of new building.



Pouring concrete stem walls.



Entry/admin and gym area concrete slab preparation.

Construction Webcam



Upcoming Activities

- Next steel delivery September 12th
- Concrete pour September 14th to complete first floor
- Metal decking delivery September 17th
- Erecting steel



Concrete pump truck with crew pouring slab.



First steel deliveries - 2 of 2 loads.

- In addition to the live webcam as shown below, a new monthly communication tool has been launched.



Webcam view of the project. Images update every 15 minutes, and a time-lapse video will be available at the end of construction.
<https://www.hoodriver.k12.or.us/Domain/456>

Mid-Valley Elementary School



- Modular interior renovation complete. Pre-School operating out of modular now.
- Cabinet completion is on-going. Majority of cabinet work for new library space has been installed.
- Playground encountered shallow gas line. Work to extend a few more weeks.



Hood River Middle School

2001 Roofing Project

- New roof ventilation, shingles and copings are wrapping up. Roof inspection and punchlist to follow.



Parkdale Elementary School


- Playground completion is scheduled for September 21.



Hood River Valley High School



- Roof replacement / repairs / siding to be complete by end of September.
- Cabinet work continues and is expected to be completed by end of September.
- Cooling system being commissioned this week.

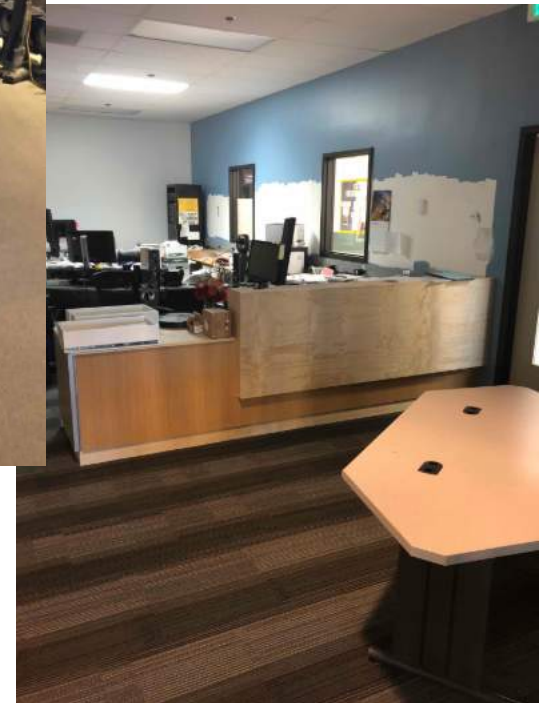

HRVHS – Henderson Community Stadium



- Installation of synthetic turf field is complete.
- Installation of synthetic track starting the week of 9/17, approximately 2.5-weeks of work.
- Perimeter fencing, sidewalks, and landscaping underway in preparation for 10/5 football game.



Hood River County School District



Pending Projects

- Parkdale Elementary School
 - Summer 2019
- Westside Elementary School
 - Summer 2019
- Mid Valley Elementary School – Seismic Upgrades
 - Summer 2019
- Pine Grove – Misc. Improvements
 - Summer 2019
- Cascade Locks Elementary School
 - Summer 2019
- Transportation Yard Paving
 - Summer 2019

Considering Additional Projects

- HRVHS Engineering Classroom
- HRVHS Additional Parking
- Expanded Roof and Soffit Repairs at Cascade Locks
