

Hood River County School District – 2016 Bond Projects


Bond Projects Report

October 2017


WENAH
GROUP

Mid-Valley Elementary

- Design and Estimating – Complete January 2018
- Considering Modular Placement and Conversion of Gym Basement to Library.
- Permit/Bid – February 2018
- Construction/Re-Roofing – April 2018 to October 2018

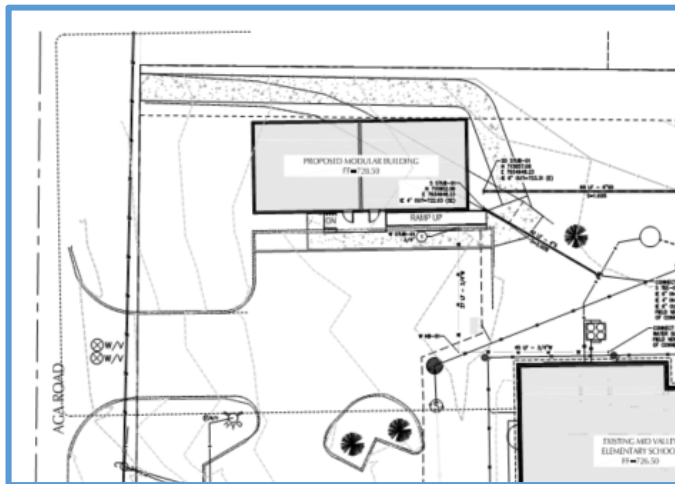

Modular Location for Pre-K
at NW Corner of Site

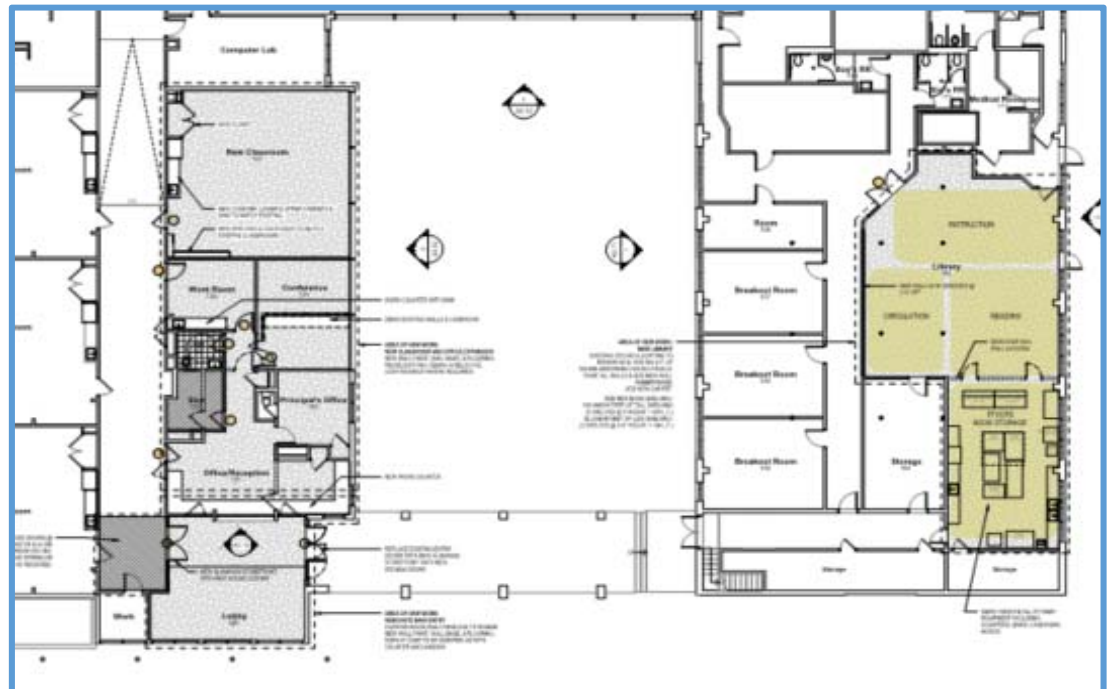

Lobby/Admin/Classroom and Library Concepts

Wy'east Middle School

- STEAM Addition Completion Scheduled for Spring Break 2018
- Seismic Grant Design (Gymnasiums) underway. Reviewing options and costs to create an “Essential Facility” – Construction 2018
- Re-Roofing – April 2018 to August 2018 – bidding next month



STEAM Addition Footings



New Bus Loop



New Canopy, Steps and Ramp Almost Done

May Street Elementary

- Bidding & Permit Drawings – Scheduled for November 17, 2017
- Temporary Playground Underway
- Construction Start – February 2018
- Completion – August 2019



Interior Finishes
Discussions and
Virtual "Walk-Through"



Hood River Valley High School

- In Design Development Phase
- Bid/Permit Documents Scheduled for January 2018
- Working Towards Early Chiller Order
- Construction/Re-Roofing – April 2018 to November 2018
- Track and Field – May 2018 to August 2018

Metal Building (Equipment and Fuel)

- Complete by mid-November 2017



Hood River Middle School:

- Completion of Renovations Scheduled For End of October 2017
- Seismic Grant Roofing and Related Fascias and Soffits to be Complete By Mid-November 2017
- Re-Roofing Cafeteria/Classroom Building – April 2018 to August 2018

Cascade Locks Elementary School:

- Security Improvements – December 2017
- Roofing Repairs/Misc Work – April 2018 to June 2018

Westside Elementary School:


- Design- February 2018 to July 2018
- Permit/Bid – December 2018 to January 2019
- Construction/Re-Roofing – April 2019 to October 2019
- Softball Batting Facility – Bid Result

Parkdale Elementary School:

- Fitness Trail This Fall – Rotary Club Project – Work Parties Scheduled
- Design- February 2018 to July 2018
- Playground Construction – June 2018 to August 2018
- Permit/Bid – December 2018 to January 2019
- Construction/Re-Roofing – April 2019 to October 2019

HRCSD Administration / Alt Ed

- Construction /Permit Documents – End of 2017
- Lump Sum Bid Process
- Construction – Feb 2018 through August 2018

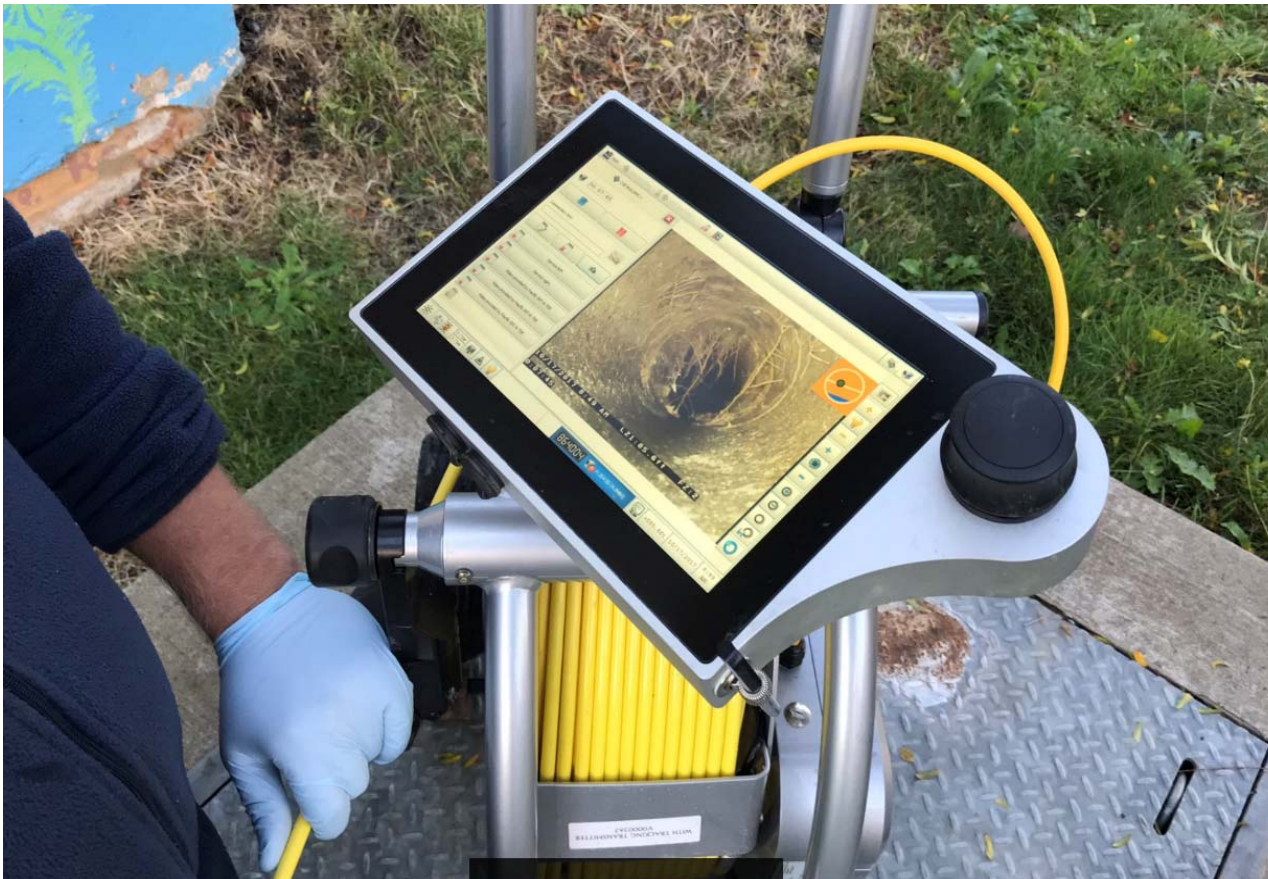

Investigating a
Lingering
Challenge at the
District Office
Site:

70-Year Old
Concrete Sewer
Pipes
