


Bond Projects Report

April 2018

Cascade Locks Elementary School

- Classroom lockset change-out Summer 2018.
- Music Room Repairs Summer 2018.
- Electronic Access Control is under design.
- Gutter, soffit and roofing repairs Summer 2019.
- Entry Canopy revisions Summer 2019.
- Playground repairs Summer 2019.

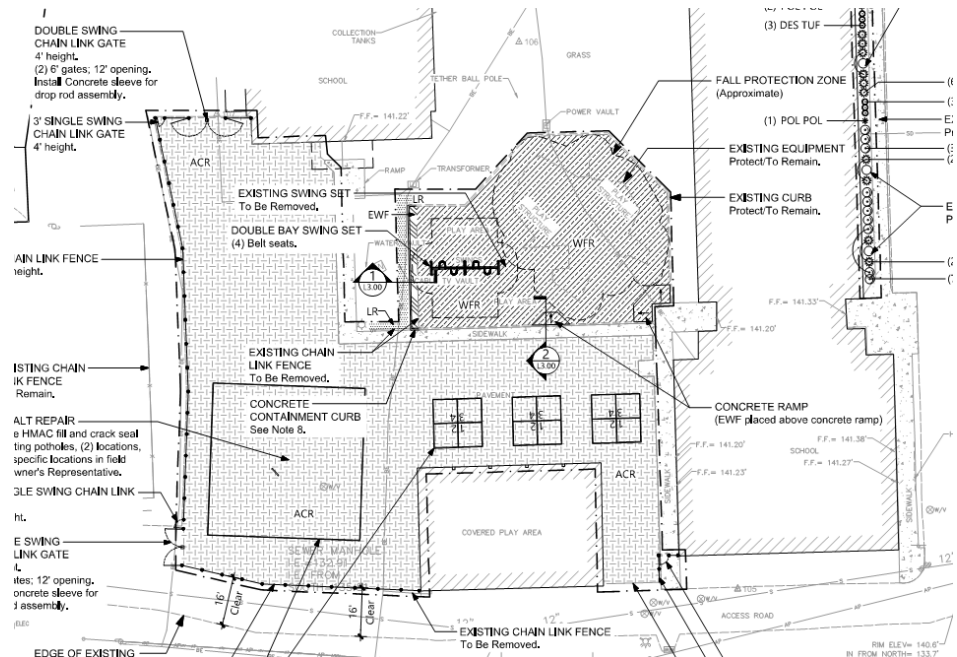

Wy'east Middle School

- STEAM Addition - Open for teaching! Site Concrete and Landscaping in process.
- Gym Seismic starts early May. School able to give the contractor half during school.
- Re-Roofing – Starting in May.
- Working towards constructing driveway late Spring – at Fairgrounds property line.



New Commons Area

Wy'east Middle School



Maker Space




“STEAM”!



New Lab Space

Parkdale Elementary School

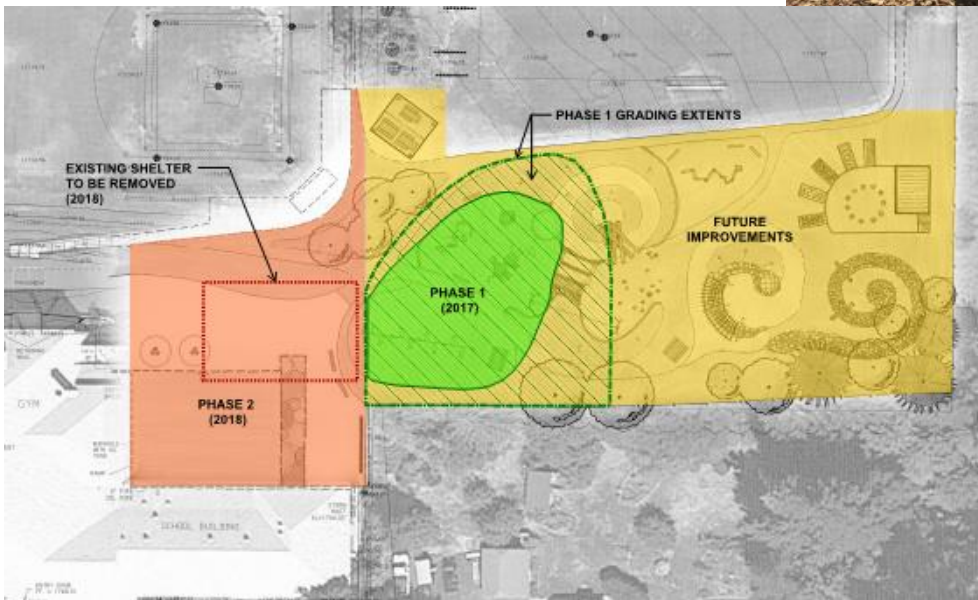

Rotary Club New Fitness Trail!

Design has started for the Parkdale Building renovations and new Covered Play Structure. Work on this phase to start 2019.

Phase 1 (Bond) Playground Replacement this summer

Coe / Alt Ed Remodel



- Construction progressing on schedule for completion late July.
- Staff will transition to Coe prior to start of Alternative School start.
- Alternative School completion scheduled for October.

Westside Elementary School

- Design - April 2018 to November 2018.
- Security Hardware improvements Summer 2018.
- Permit/Bid – December 2018 to January 2019.
- Construction/Re-Roofing – April 2019 to October 2019.



Hood River Middle School

- Re-Roofing Cafeteria/Classroom Building – April 2018 to August 2018.
- Additional Classroom Lockset Changes and Added Access Control this summer.



Mid Valley Elementary School

- Permit application submitted late February.
- Learning Garden is being relocated by volunteers.
- Construction/ Re-Roofing – June to September 2018.
- Preparations for the modular installation will begin in May.



Modular from May Street Temporarily Stored at Mid-Valley Parking Lot. To be set this summer.

Hood River Valley High School

- Baseball Netting System installed at JV Field to protect cars at the Golden Eagle Park.
- Temporary Stair Towers for Roof Access will be installed early May.
- Construction/Re-Roofing – May to October 2018.
- Track and Field – May 7, 2018 to September 30, 2018.



Districtwide Security Enhancements

- Remaining classroom lockset change-outs for this summer:
 - Cascade Locks Elementary
 - Westside Elementary
 - Parkdale Elementary
 - Mid-Valley Elementary
 - Pine Grove School
 - Hood River Valley High School
- Lockset Process Timeline
 - Site Surveys by Wenaha Group complete 4/20/18.
 - Hardware specified by consultant 5/11/18.
 - Release for order / procure hardware 5/18/18.
 - Receive hardware by 7/13/18.
 - Begin installation of hardware 7/16/18.
 - Complete hardware installation 8/31/18.
- Additional Security Enhancements
 - Electronic Access Control (EAC) design is underway for all remaining schools with goal of completion this year.
 - There will be further enhancements 2019 with some entry vestibules.
 - Adding Security Film at key glass points is being investigated.

May Street Elementary School

- Construction Underway – On schedule to be open for Fall 2019.



Webcam view of the project. Images update every 15 minutes, and a time-lapse video will be available at the end of construction.

<https://www.hoodriver.k12.or.us/Domain/456>
